



Republic of the Philippines
JOSE RIZAL MEMORIAL STATE UNIVERSITY
College of Computing Studies
Main Campus, Dapitan City



TEAMTALK: A Canva-Themed Messenger

Submitted to:

MR. CHARLIE BAGUIO
CCS Instructor

Submitted by:

GROUP 2

ABAL, CHE ANN P.

ANTIPUESTO, LEO ALFIER S.

ANTIVO, ROVILL S.

JACALAN, KHENT BRYAN M.

JUMALON, REYMARD G.

LAGPAC, SHEILA MAE A.

ORIA, MELISSA A.

May 18, 2026

TABLE OF CONTENTS

Executive Summary	1
I. Project Requirements (SRS).....	1
1.1 Project Design Philosophy and Focus.....	1
1.2 Client Consultation	2
1.3 Identity and Access Management	3
1.4 Functional Requirements (Must-Haves)	3
1.5 Secondary Features (Stretch Goals).....	3
1.6 Non-Functional Requirements	3
1.7 Scope Exclusions and Strategic Deferral	4
II. Project Management & Estimation.....	5
2.1 Role Assignments and Contributions.....	5
2.2 Project Effort Estimation & Baselining (Baseline 1.0).....	6
2.3 Project Re-baselining & Impact Analysis (Baseline 1.1)	7
III. System Architecture	9
3.1 Architectural Overview.....	9
3.2 Tiered Structure and Responsibility.....	10
3.3 Strategic Data Flow Mechanisms	13
IV. Communication Challenges and Proposed Strategies.....	13
V. Project Plan: Gantt Chart & Notion Board	15
5.1 Gantt Chart (5-Week Agile Roadmap)	15
5.2 Monitoring Method: Integrated Project Hub (Notion).....	16
VI. Detailed Agile Sprint Schedule.....	17
Appendix A: Minutes of Meeting — Kickoff & Pre-Sprint (April 10)	20
Appendix B: Minutes of Meeting — Scope Revision (April 14)	24
Appendix C: Final Quality Analysis (May 16)	29

Executive Summary

This document presents the full project management plan for TeamTalk — a standalone, Canva-themed real-time messaging application designed specifically for design teams. The goal is to deliver a functional Minimum Viable Product (MVP) within a 5-week development window, targeting submission by the week of May 11–14.

TeamTalk addresses a core productivity gap: Canva users currently rely on external communication tools (Messenger) while designing, forcing constant context-switching that disrupts creative flow. TeamTalk solves this by providing a collapsible chat sidebar or standalone window that keeps the team communicating and designing in the same visual environment.

The MVP scope is focused on three core features: real-time messaging, asset drag-and-drop (directly from chat onto the canvas), and voice recording for quick feedback. Secondary features — including an AI-powered Magic Summary and Team Polls — are scoped as stretch goals to protect the May deadline.

The development of TeamTalk is centered on solving the high-latency communication gap within the Canva environment. Unlike standard administrative tools, this project prioritizes Bi-directional Real-Time Interaction and Technical Performance (NFR6). The engineering effort is intentionally concentrated on the "Primary Technical Value Drivers"—specifically the WebSocket messaging engine and the coordinate-persistent canvas integration—rather than secondary administrative modules such as exhaustive collaborator management or tiered authorization levels.

The team of seven operates across six defined roles: Project Manager, Frontend Developer, Backend Developer, UI/UX Designer, Asset/Brand Designer, Tester, and Client. Development follows a parallel workflow supported by a Notion workspace for task tracking and a 5-week sprint plan with built-in risk mitigation strategies.

I. Project Requirements

1.1 Project Design Philosophy and Focus

The development of TeamTalk is centered on solving the high-latency communication gap within design environments. In a high-velocity 5-week sprint, the team adopted a **Technical Value-First** philosophy. We prioritized the development of bi-directional real-time sync (NFR6)

and complex UI-state management (FR2). This ensures the prototype validates the most difficult engineering challenges of the system first.

The system utilizes an **Activity-Based Discovery** model. To maintain a 'Clean Canvas' environment and reduce background WebSocket overhead, collaborator presence is identified through active participation (messaging or asset interaction) rather than a persistent idle-user list. This ensures that the interface remains focused on active creative contributions.

1.2 Client Consultation

Before any design or coding began, the Project Manager conducted a Requirement Discovery session with the Client to baseline the project scope. The goal was to ensure the "TeamTalk" features directly solved the communication gaps in Canva.

Evidence of Client Consultation:

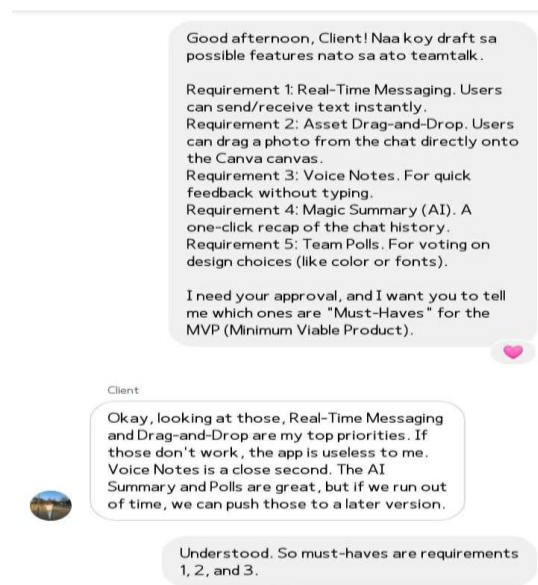


Figure 1. Stakeholder consultation between the PM and Client (Rovill) to prioritize functional requirements and lock the MVP scope.

1.3 Identity and Access Management

- **Persistent User Authentication:** To ensure data integrity and security, TeamTalk includes a User Account Tier (Login/Sign-up). This allows the system to verify collaborators before they access the collaborative workspace.
- **Identity-Aware Session Logic:** Upon successful authentication, the system automatically retrieves the user's profile data. This identity is dynamically bound to the Room ID during room creation or entry, eliminating manual name-entry and ensuring that every message in the real-time feed is accurately attributed to a verified collaborator.
- **Implicit Presence Indicators:** Collaborator identity is revealed dynamically through the real-time feed. By binding the User Identity to the Socket.IO payload, the system ensures that every interaction (Chat/Drag-and-Drop) serves as a simultaneous 'Presence Heartbeat,' confirming the user's active status within the room.

1.4 Functional Requirements (Must-Haves):

- **FR0: Collaborative Authentication Tier** — The system shall provide secure Sign-up and Login functionality to establish a persistent user identity.
- **FR1: Real-Time Messaging:** Instant text communication in a persistent feed visible to all project collaborators.
- **FR2: Asset Drag-and-Drop:** Users can drag images from the chat directly onto the integrated simulated canvas.
- **FR3: Voice Recording:** A microphone button for quick audio feedback.

1.5 Secondary Features (Non-Priority/Stretch Goals):

- **FR4: Magic Summary (AI):** One-click AI recap of missed chat history.
- **FR5: Team Polls:** Interactive voting on design choices (colors, fonts).

1.6 Non-Functional Requirements

- **NFR1 (Usability):** The UI must strictly adhere to Canva's Design System (Inter Font, #00C4CC palette, and 8px rounded corners) to ensure a zero-learning curve for existing Canva users.
- **NFR2 (Reliability):** The system must include a "Safety Save" feature that automatically backs up chat history to the cloud every 5 seconds to prevent data loss during internet flickers.

- **NFR3 (Usability):** The TeamTalk sidebar must be collapsible to allow users to maximize the design workspace during periods of deep focus.
- **NFR4 (Compatibility):** The standalone app must be fully responsive, functioning correctly on the latest versions of Chrome, Safari, and Edge without any UI "breaking."
- **NFR5 (Maintainability):** The codebase must be modular so that secondary features (like Magic Summary) can be integrated in Week 5 without requiring a rewrite of the core chat engine.
- **NFR6 (Performance/Sync):** The system must utilize WebSockets to ensure that messages and asset drops are synchronized across all active collaborator screens in under 1 second.

1.7 Scope Exclusions and Strategic Deferral

To ensure the stability of the WebSocket tunnel and meet the May 11–14 deadline, the following features are classified as deferred for future versions:

- **Persistent Collaborator Directories:** While the system includes a Sign-up/Login tier to verify identity, the ability to browse a global directory of all registered users is deferred. This version utilizes Dynamic Room Logic, where users are identified only upon joining a specific Room Code, focusing resources on session isolation.
- **Tiered Permissions (Admin/Editor/Viewer):** To optimize creative flow and rapid prototype testing, the system assumes a flat "Collaborator" role. All authenticated users within a Room share equal editing and messaging privileges.
- **Passive Presence Indicators (Online/Offline Status):** Replaced by Activity-Based Discovery. To prioritize the NFR6 sub-1 second latency requirement for active data transmission, the system does not poll for "idle" users. Collaborator presence is established through active interaction with the messaging feed or canvas.

II. Project Management & Estimation

2.1 Role Assignments and Contributions

The team consists of seven members covering five core roles: Project Manager, two Designers, two Developers, a Tester, and a Client. The split ensures that design and development can run in parallel without either track waiting on the other.

Role	Assigned Member	Specific Responsibilities & Contributions
Project Manager	Melissa A. Oria	Leads the team as the central point of contact. Creates the Gantt chart, tracks milestones, and bridges communication between the Client and the technical team. Responsible for setting sprints, managing the Notion board, and enforcing the 24-hour rule to prevent bottlenecks.
Designer 1 (UI/UX)	Khent Bryan M. Jacalan	Designs the project entry landing page, the TeamTalk interface layout and the simulated canvas drop zone. Responsible for the visual flow of the chat window, input bar, mic button, and drag-and-drop area. Produces wireframes and high-fidelity mockups that serve as the developer's visual reference before coding begins.
Designer 2 (Asset & Brand)	Reymard G. Jumalon	Designs custom icons and ensures the entire TeamTalk interface and landing page matches Canva's design system — applying the color palette, Inter typography, and button styles so the app feels like a native Canva product.
Developer 1 (Frontend)	Sheila Mae A. Lagpac	Builds the TeamTalk chat interface using the approved mockups as reference. Responsible for frontend coding, collapsible sidebar, real-time chat engine development, and integrating the drag-and-drop asset feature and voice note functionality.
Developer 2 (Backend)	Leo Alfier S. Antipuesto	Manages the Real-time Messaging Engine and Room Logic. Responsible for setting up the server so that multiple users can communicate within the same Room Code. Handles backend logic for voice note storage and asset management, and collaborates with Developer 1 during feature integration in Week 3.
Tester	Che Ann P. Abal	Conducts incremental unit and integration testing from Week 3 onward. Verifies real-time sync (<1s), canvas asset handoff, and sidebar responsiveness. Performs full system testing in Week 4, including stress tests and end-to-end scenarios, to ensure the app is stable before submission.
Client	Rovill S. Antivo	Provides the Product Requirements Document and defines Must-Have features versus stretch goals at kickoff. Reviews and approves all designs by end of Week 1 and performs final User Acceptance Testing (UAT) in Week 5 before submission.

Evidence of Role Allocation:

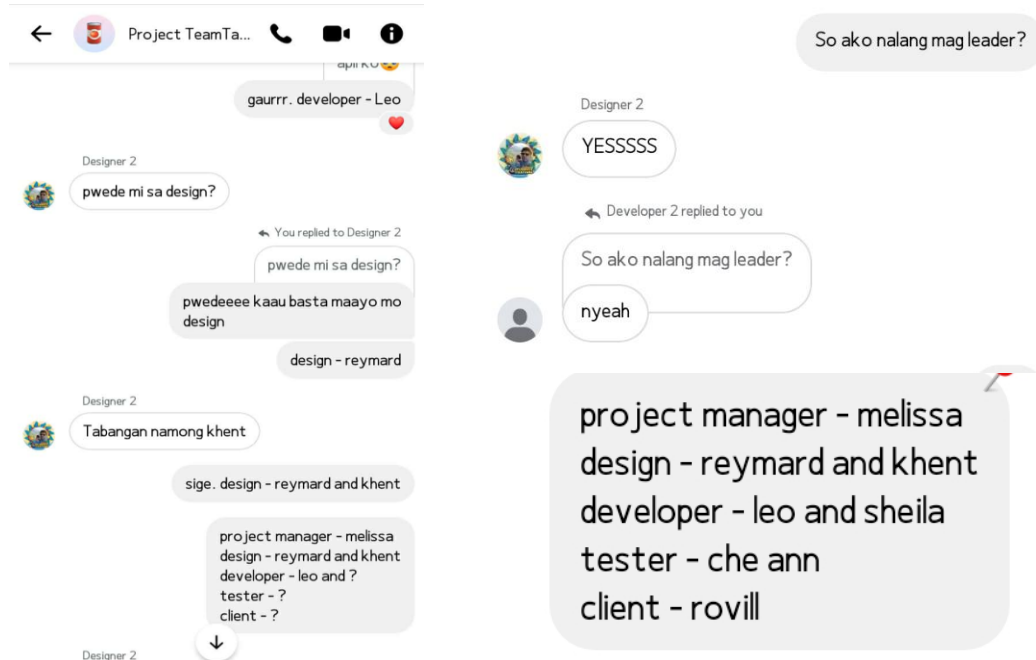


Figure 2.1 Messenger discussion regarding team strengths and final role assignments.

2.2 Project Effort Estimation & Baseline (Initial Expert Judgment)

2.2.1 Initial Effort Estimation (Baseline 1.0)

To predict the project's total effort, the PM conducted an estimation session using Expert Judgment. By consulting the technical leads (Developers) and creative leads (Designers), the total effort was baselined at **95–100 man-hours** over a 6-week window.

Estimation Logic & Milestone Schedule:

- **Pre-Sprint:** Kickoff Meeting & Role Assignment
- **Week 1:** Requirement baselining and UI/UX Mockup finalization (Design-heavy).
- **Week 2:** Environment setup and Frontend development.
- **Week 3:** Core Chat Engine development (Backend/Real-time sync).
- **Week 4:** Feature Integration (Asset Drag-and-Drop and Voice Note logic).
- **Week 5:** System Testing & QA; Secondary features (Magic Summary/Polls) pursued only if time permits.

- **Week 6:** Final Buffer for bug fixing, documentation polish, and submission.

Evidence of Initial Process:

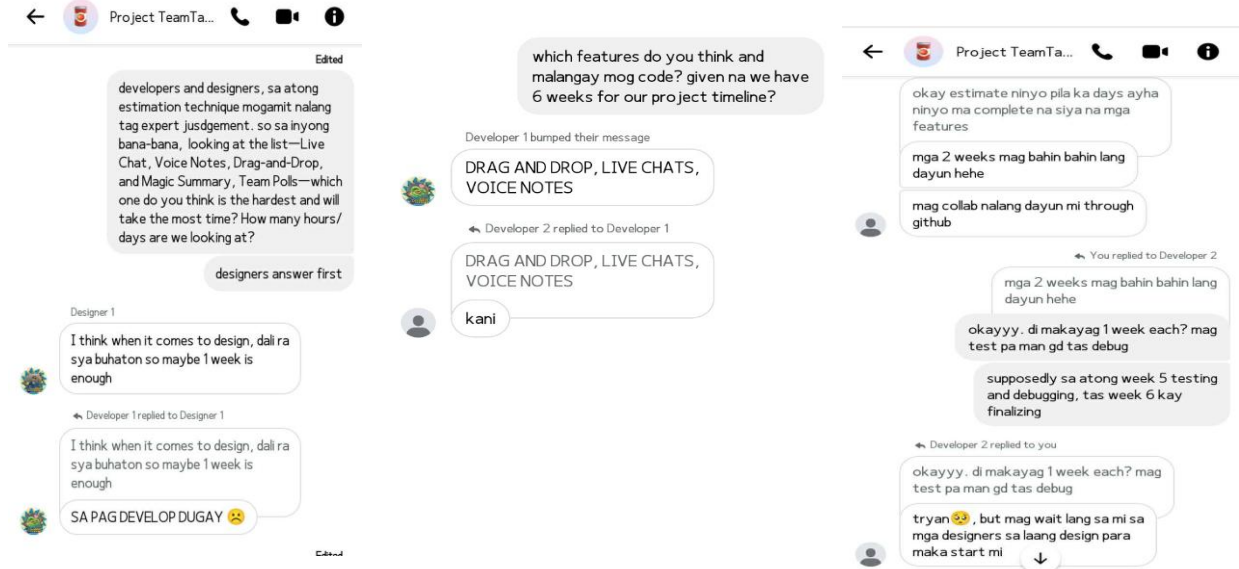


Figure 2.2 Figure 1: Initial Expert Judgment Session (6-Week Target)

2.3 Project Re-baselining & Impact Analysis (Baseline 1.1)

Trigger for Revision: Due to a timeline compression from 6 weeks to 5, the PM conducted a second **Expert Judgment session** on **April 14, 2026** to assess the feasibility of a high-velocity delivery.

Revised Estimation Logic:

To maintain a high standard of technical quality within the shortened window, the team performed a Technical Impact Analysis and opted for a **200 Total Man-Hour Baseline**. This re-estimation ensures that the core features are not just functional but "production-ready." The strategy includes:

- **Pre-Sprint Baselining:** The Requirement Baseline was moved to the Pre-Sprint phase to ensure "Day 1" of Week 1 is dedicated to execution rather than planning.
- **Intensive Resource Loading:** Increasing the Developer effort to 150 hours (averaging ~3 hours daily per developer) to handle the complexity of the real-time engine and canvas integration.

- **Strategic Allocation:** Dedicating 20 hours for UI/UX Design (concentrated in Week 1) and 20 hours for System Testing/QA (concentrated in Week 4) to protect the product's integrity.
- **Management Oversight (10h PM):** 10 hours are reserved for the PM to manage the Notion board, enforce the 24-hour rule, and handle communication, preventing technical bottlenecks.
- **Parallelization:** UI/UX Design and Backend Architecture (Environment/DB) now run concurrently in Week 1 to maximize output.
- **Scope De-prioritization:** To mitigate risk, "Stretch Goals" (Magic Summary and Polls) were moved to a conditional status, ensuring 100% focus on the Core MVP features.

Revised Milestone Schedule (5-Week Cycle):

- **Pre-Sprint:** Kickoff Meeting, Role Assignment, and Requirement Baselineing.
- **Week 1:** Design & Foundation (UI/UX Mockups & Database Setup).
- **Week 2:** Frontend Coding & Core Chat Engine Development.
- **Week 3:** Feature Integration & Incremental Unit Testing.
- **Week 4:** System Testing (Code-Complete Deadline).
- **Week 5:** UAT, Bug Fixing, and Final Submission.

Consensus Validation:

The technical leads reviewed the revised task dependencies and confirmed that the core MVP is achievable within the 5-week duration. The total effort remains baselined at **200 man-hours**, distributed with higher intensity across the mid-sprint phases.

Evidence of Project Re-baselining:

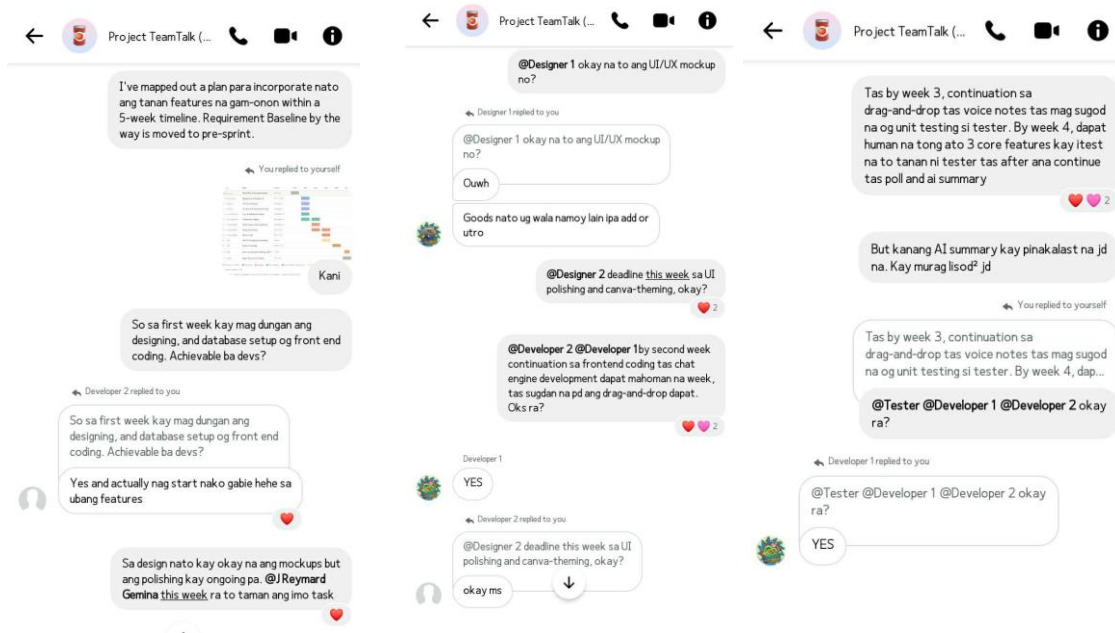


Figure 2.3 Evidence of Technical Consensus on Revised 5-Week Timeline

III. System Architecture

3.1 Architectural Overview

To meet the high-velocity requirements of the 5-week sprint and the technical mandates of the SRS, TeamTalk utilizes a Decoupled 3-Tier Client-Server Architecture. This pattern is selected specifically to allow for Concurrent Engineering; enabling the frontend and backend teams to develop, test, and iterate on separate layers of the system simultaneously.

3.2 Tiered Structure and Responsibility

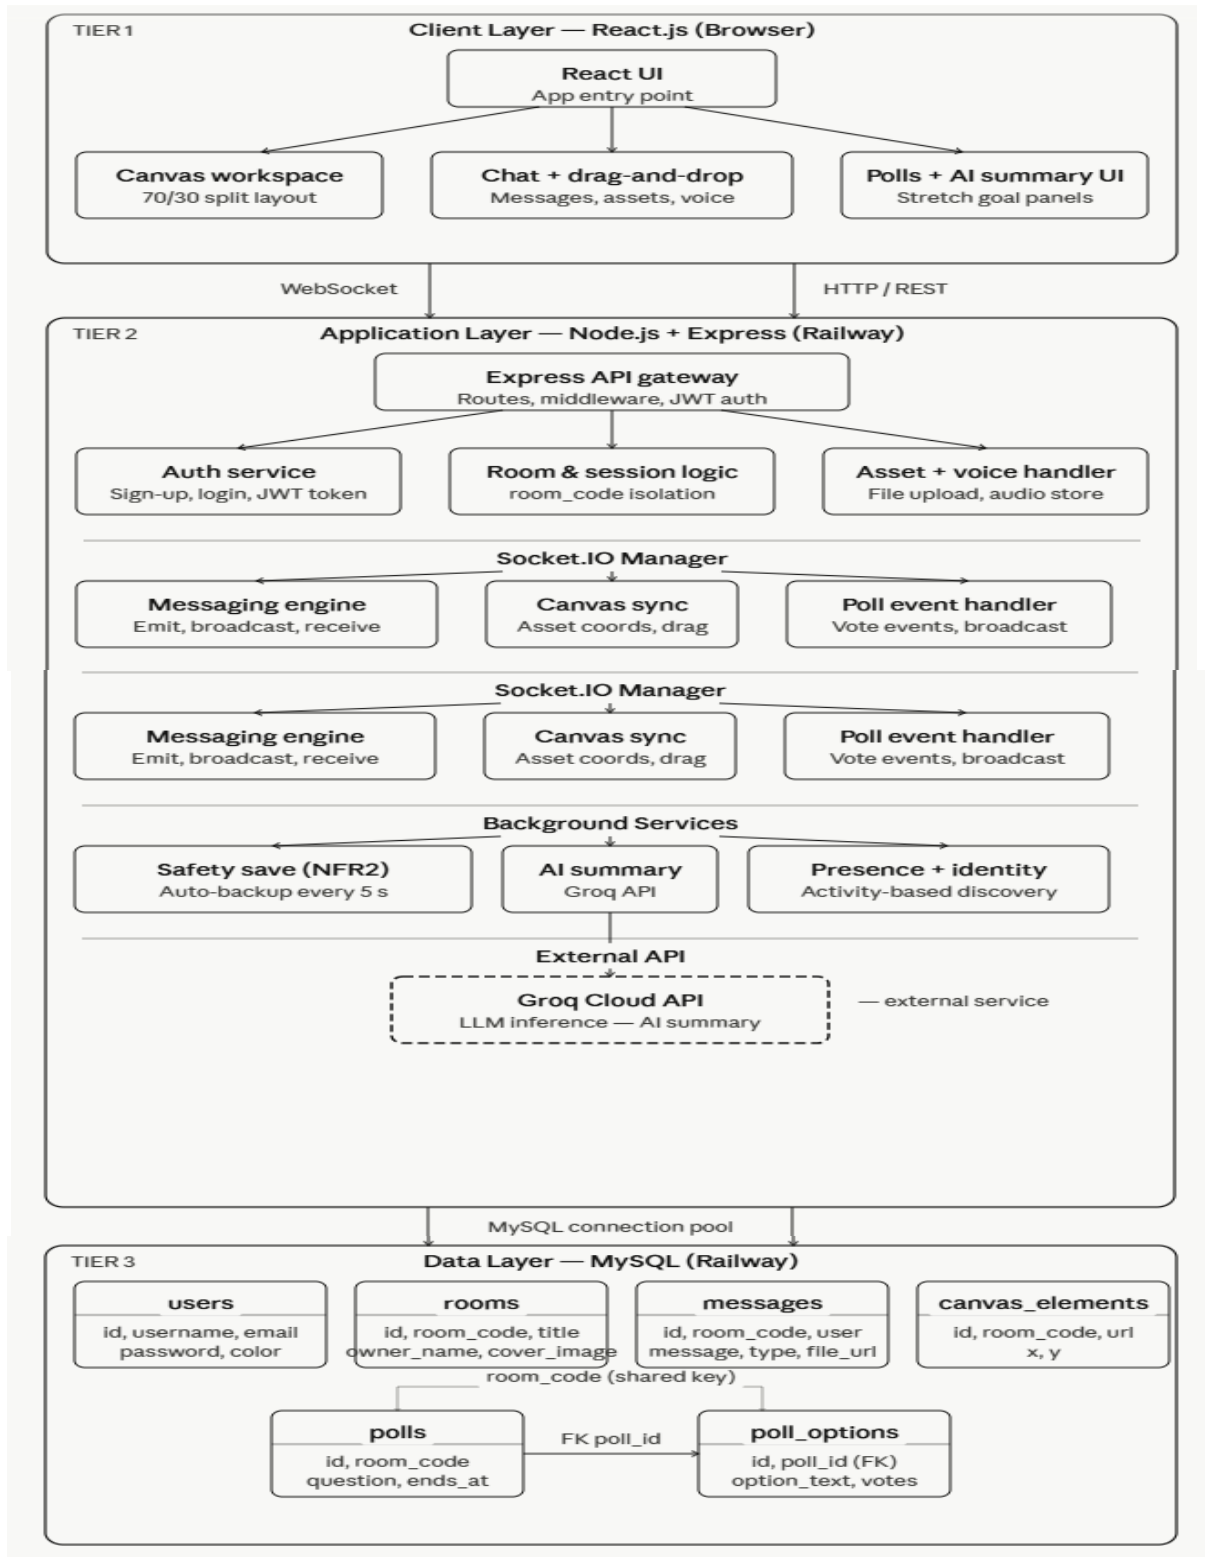


Figure 3: TeamTalk 3-Tier Integrated System Architecture

Tier 1: Presentation Layer (Frontend – React)

The Presentation Layer acts as the primary interface and event-source for the system.

Technology: React.js.

Key Responsibilities:

- **UI Orchestration:** Rendering the Canva-themed interface with a 70/30 split workspace, enforcing Canva's brand alignment (NFR1) and supporting a collapsible sidebar to maximize the design workspace (NFR3).
- **Event Handling:** Capturing user actions such as text input, photo uploads, microphone activation for voice notes (FR3), and coordinate-based asset drag-and-drop onto the canvas (FR2). Stretch goal panels for Team Polls and AI Magic Summary are also housed in this layer (FR4, FR5).
- **Real-time Consumption:** Maintaining an active listener on the Socket.IO tunnel to update the chat interface, canvas state, and poll results instantly without page refreshes (NFR6).

Tier 2: Application Layer (Logic – Node.js & Express)

The Application Layer serves as the "System Brain," orchestrating the movement of data between users and storage.

Technology: Node.js + Express API, deployed on Railway.

Key Responsibilities:

- **Express API Gateway:** Handles all inbound HTTP/REST requests, applying routing middleware and JWT-based authentication to verify collaborator identity before granting access to any room or feature.
- **Auth Service:** Manages user sign-up, login, and session token issuance, binding a verified identity to every Socket.IO payload so that all messages and canvas interactions are accurately attributed.

- **Room & Session Logic:** Manages session isolation using `room_code` as the shared key, ensuring that messages, canvas elements, and poll events are only broadcast to clients within the same project room.
- **Asset & Voice Handler:** Processes file uploads and audio recordings, storing references for retrieval by collaborators within the same room.
- **Socket.IO Manager:** Maintains the bi-directional WebSocket communication tunnel across three engines — the Messaging Engine (emit, broadcast, receive), the Canvas Sync Engine (asset coordinates and drag events), and the Poll Event Handler (vote events and result broadcast) — ensuring sub-1 second synchronization (NFR6).
- **Background Services:** Runs three asynchronous processes independently of the live chat stream: the Safety Save protocol (NFR2), which auto-backs up chat and canvas state every 5 seconds; the AI Summary service, which queries chat history and calls the Groq Cloud API for LLM inference; and the Presence & Identity service, which tracks active collaborators through activity-based discovery rather than idle polling.

Tier 3: Data Layer (Persistence – MySQL)

The Data Layer provides the system's permanent memory and state recovery capabilities.

Technology: MySQL, hosted on Railway.

Key Responsibilities:

- **History Persistence:** Storing every message (including type, file references, and reply threading) and canvas element coordinate via the `messages` and `canvas_elements` tables, ensuring full room history is available for late-joining collaborators.
- **User & Room Management:** The `users` table persists authenticated identities, while the `rooms` table stores project metadata including `room_code`, cover image, and visit/edit counters.
- **Poll Persistence:** Poll questions are stored in the `polls` table, with each choice and its running vote count maintained in the linked `poll_options` table via a foreign key relationship.

- **Safety Save Protocol (NFR2):** Automated writes to the messages and canvas_elements tables execute every 5 seconds asynchronously, minimizing data loss in the event of client or server disconnection.

3.3 Strategic Data Flow Mechanisms

3.3.1 Bi-directional Real-Time Sync

Unlike traditional HTTP request-response cycles, TeamTalk utilizes a persistent WebSocket tunnel via Socket.IO. When an event occurs — a message sent, an asset dropped onto the canvas, or a Vote Event triggered — the data is emitted directly to the Application Layer's Socket.IO Manager, which immediately broadcasts the change to all other clients sharing the same room_code. This mechanism is the primary driver for achieving the sub-1 second sync requirement (NFR6).

3.3.2 Asynchronous State Management

To ensure the real-time messaging engine remains high-performance, the Safety Save and AI Query processes operate asynchronously via the Background Services module. The Safety Save writes to the messages and canvas_elements tables every 5 seconds without blocking active socket events. The AI Summary service independently queries MySQL for historical chat logs, forwards them to the Groq Cloud API for LLM inference, and broadcasts the generated summary back through the Socket.IO Manager — all without interrupting the active live chat stream.

IV. Communication Challenges and Proposed Strategies

Conflict and miscommunication are inevitable in any team project, especially under a tight deadline. The following challenges were identified in advance, along with practical strategies to prevent them from derailing the timeline.

Challenge	Root Cause & Impact	Proposed Strategy
1. Internet Connection Issues	Members may experience unstable or lost internet connections, causing missed messages, delayed file uploads, and gaps in real-time collaboration that can stall the entire team's progress.	Daily GitHub Pushes: All work must be uploaded to GitHub daily so teammates can access the latest version even if a member goes offline. The PM is notified immediately of any prolonged disconnection.
2. Designer-Developer Gap	Designer may produce a visually ambitious mockup that is technically infeasible within a 5-week window.	Enforce a 24-Hour Reality Check rule: After every mockup is shared, Developers have 24 hours to flag technical concerns before any coding begins.
3. Client Scope Creep	The Client may add feature requests mid-sprint (e.g., 'Let's add video editing too!'), causing deadline slippage, developer overload, and misaligned priorities.	Lock scope after Week 1 approval. Any new request is logged in a Post-MVP Backlog in Notion. The PM reviews all change requests. No feature is added without an impact assessment.
4. Poor Task Coordination	Without clear task ownership, members may duplicate work or accidentally leave tasks unattended, wasting time and risking missed deliverables.	Notion Ownership Rule: Every task must have one assigned owner before work begins. The PM checks the board daily to catch overlaps or unassigned tasks early.
5. Unequal Workload Distribution	Developer 1 holds the most technically complex task (the Drag-and-Drop Asset), while other team members may finish earlier and sit idle, creating a pace imbalance that delays integration.	The PM does a weekly workload check and redistributes tasks as needed.
6. Delayed Client Approvals	Late client reviews create a bottleneck that stalls coding and asset integration, putting the entire 5-week schedule at risk.	A 24-hour approval SLA is enforced from Week 1, and if the client remains unreachable by day 2, the team moves forward using the last approved version.
7. Integration Failures in Week 4	When Developer 1 (frontend) and Developer 2 (backend) merge their codebases in Week 4, integration issues such as mismatched API formats or conflicting logic may surface and cause significant rework.	Developers agree on data contracts in Week 2. Use a shared staging branch on GitHub and start integration checks in Week 3.
8. Free-Riding	A member may consistently miss meetings, ignore assigned tasks, and leave their workload to teammates — creating an unequal burden on the rest of the team and threatening the quality and timeliness of the entire project.	3-Strike Policy: The PM documents each instance of non-participation. A formal warning is issued on the 1st and 2nd violation. On the 3rd strike, the member is removed from the team and the Client is notified. All absences and missed tasks are logged in Notion as evidence.

Evidence of Conflict Mitigation Planning:

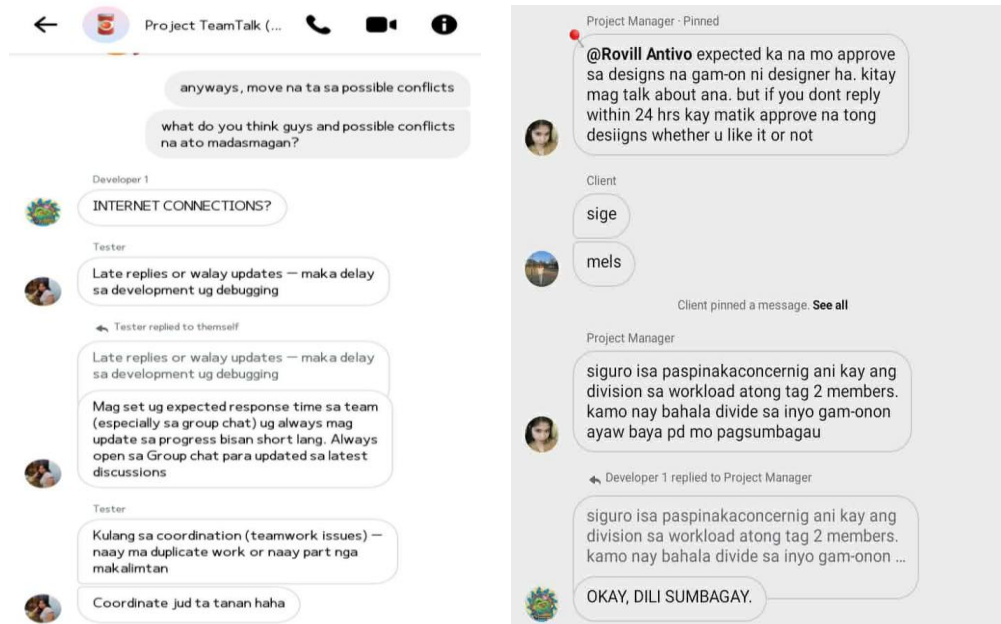


Figure 4. Group sync identifying potential bottlenecks like late replies and integration issues.

V. Project Plan: Gantt Chart & Notion Board

The project utilizes Gantt chart and Notion board to set project timeline, tasks, and monitor weekly progress. It outlines our 5-week development cycle for the TeamTalk messenger. Because we are following an Agile methodology, you'll notice that several phases overlap—specifically Design, Development and Testing. This allows the team to iterate quickly and catch bugs in Week 3 instead of waiting until the end of the project.

5.1 Gantt Chart (5-Week Agile Roadmap)

A filled colored box indicates an active work period for the given phase and owner. Empty cells indicate no scheduled work for that role in that week.

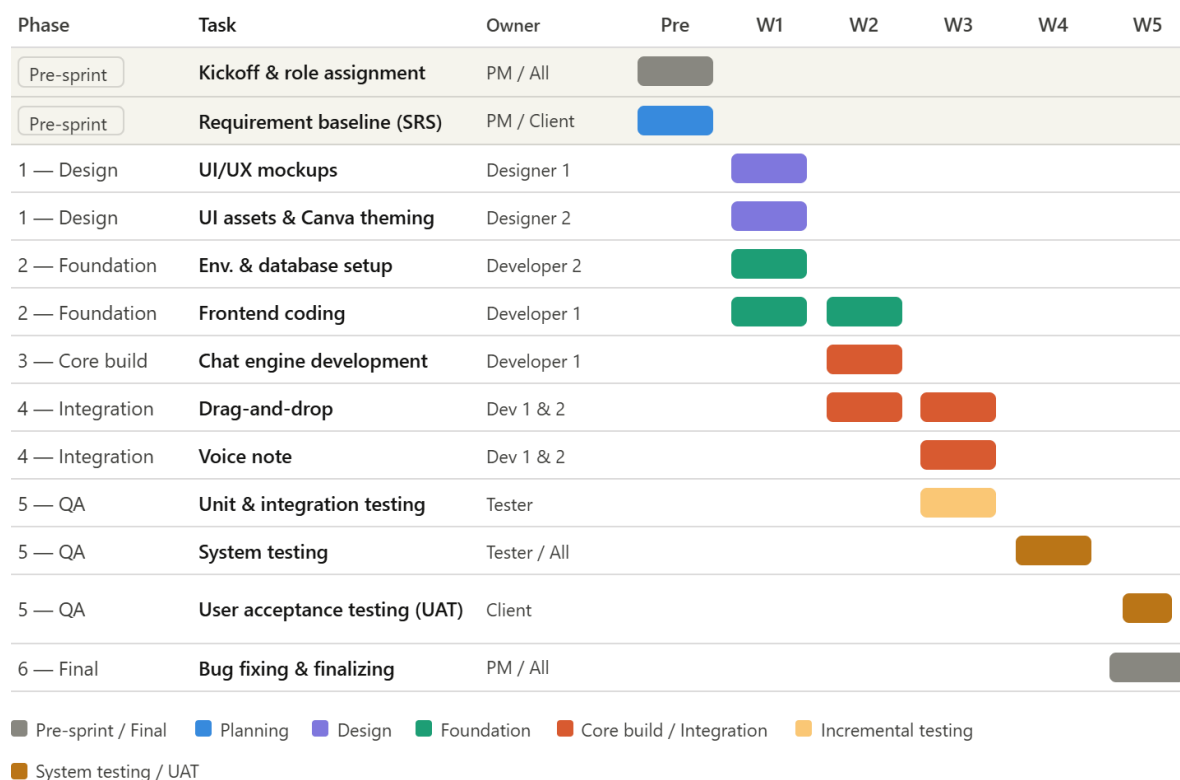


Figure 5.1 summarizes our 5-week roadmap, which we track daily in Notion to stay on schedule.

5.2 Monitoring Method: Integrated Project Hub (Notion)

To keep our project organized and in one place, we use **Notion** as our main tracking tool. Instead of using separate apps for tasks and schedules, Notion allows us to sync our task board and our timeline in one hub so everyone stays on the same page. We monitor our progress using two main views:

5.2.1. Agile Board View (Kanban)

We break down all the project requirements into small tasks on a **Board View**. This helps us see exactly how the work is moving through four stages:

- **To Do:** Tasks planned for the current week.
- **In Progress:** Tasks the team is currently working on.

- **Review & QA:** Completed tasks awaiting final sign-off. For Design tasks, this is the **Client Approval** stage. For Development tasks, this is the **Technical Testing** stage.
- **Done:** Fully approved and finished features.

5.2.2. Timeline View (Gantt Chart)

We use the Timeline View as our project's Gantt Chart. Since it's linked to the same task list, any time we change a date on the board, the chart updates automatically. This helps me, as the PM, see if tasks are overlapping correctly and ensures we are on track for the **May 11–14 submission**.

Evidence on Planning and Tool Setup:

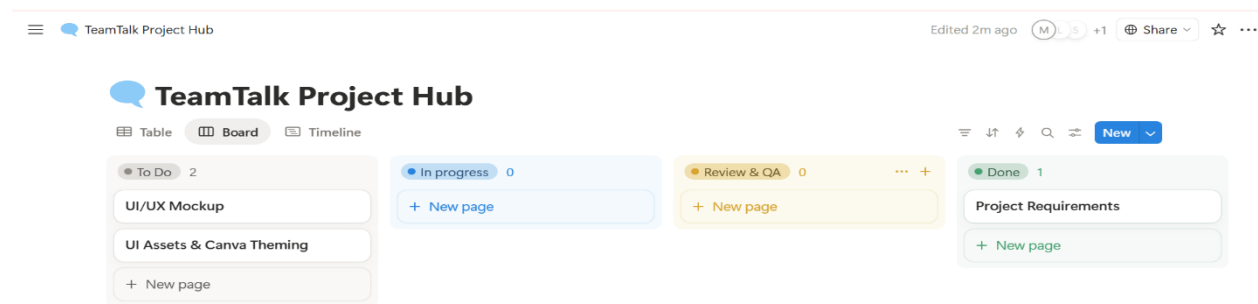


Figure 5.2 Initial Setup of the Notion Workspace

2

VI. Detailed Agile Sprint Schedule

The following breakdown provides a clear picture of what each team member is expected to accomplish in each week of the sprint.

Pre-Sprint — Kickoff, Role Assignment & Requirement Baseline

- The Client provides the requirements and defines Must-Have vs. stretch goal features.
- The PM facilitates the kickoff meeting, assigns roles, and sets up the Notion board and communication channels.
- The team discusses individual strengths and finalizes responsibilities across all six roles.

- The PM locks the MVP scope and the SRS is completed by end of Pre-Sprint, serving as the formal requirement baseline before Week 1 begins.

Week 1 — Design & Foundation

- Designer 1 produces wireframes and high-fidelity UI/UX mockups of the landing page, TeamTalk interface, and canvas drop zone.
- Designer 2 finalizes custom icons, color palette, and UI styling in line with Canva's design system.
- Developer 2 begins environment and database setup in parallel with the design phase.
- Developer 1 begins initial frontend coding once mockups are approved.
- All design outputs must be completed and approved by the Client within Week 1.

Week 2 — Frontend Coding & Core Chat Engine

- Developer 1 continues frontend coding, building the chat interface shell, landing page room entry, and the target canvas container based on approved mockups.
- Developer 1 begins chat engine development — the real-time logic that sends, receives, and displays messages instantly between users.
- Developer 2 connects the backend database to support persistent message storage.
- Both tracks run in parallel, with the chat engine built on top of the frontend shell.

Week 3 — Feature Integration & Incremental Testing

- Developer 1 and Developer 2 continue drag-and-drop asset integration — allowing users to drag images from the chat directly onto the simulated canvas.
- Developer 1 begins voice note implementation — adding the microphone button and audio recording logic.
- Developer 1 implements the collapsible sidebar toggle to maximize workspace real estate.
- Tester begins unit and integration testing — verifying that the chat engine, database connectivity, and drag-and-drop function correctly as individual components before full integration.

Week 4 — System Testing

- The Tester conducts full system testing, running end-to-end scenarios and stress tests to ensure the entire application is stable.
- Developers resolve crashes, edge-case failures, and integration bugs flagged by the Tester.
- Magic Summary (AI) and Team Polls are pursued only if all must-have features are stable and time permits.
- All features must be code-complete by the end of Week 4. This is the internal deadline.

Week 5 — UAT, Bug Fixing & Submission

- The Client performs User Acceptance Testing (UAT), validating that the delivered features meet the original requirements.
- The team resolves any remaining bugs and inconsistencies identified during UAT.
- All documentation including this plan, the Notion archive, and codebase notes are finalized.
- The project is submitted by **May 11–14**.

Appendix A: Minutes of Meeting - Kickoff & Pre-Sprint (April 10)

MINUTES OF MEETING

TeamTalk: A Canva-Themed Messenger

Kickoff / Pre-Sprint Meeting

1. Meeting Details:

Meeting Title:	TeamTalk Kickoff / Pre-Sprint Meeting
Date:	April 10, 2026 (Friday)
Time:	3:00PM-4:00PM
Location / Platform:	Online — Messenger Group Chat
Facilitator / Chair:	Melissa A. Oria (Project Manager)
Note-Taker:	Che Ann P. Abal
Next Meeting:	Week 1 — UI/UX Design & Environment Setup.

2. Attendees:

The following members were present during the Kickoff / Pre-Sprint Meeting held on April 10, 2026:

- Melissa A. Oria — Project Manager
- Khent Bryan M. Jacalan — Designer 1 (UI/UX)
- Reymard G. Jumalon — Designer 2 (Asset & Brand)
- Sheila Mae A. Lagpac — Developer 1 (Frontend)
- Leo Alfier S. Antipuesto — Developer 2 (Backend)
- Che Ann P. Abal — Tester
- Rovill S. Antivo — Client

3. Agenda:

The following items were included in the agenda for this meeting:

- Welcome and introduction of all team members.
- Project overview of TeamTalk: A Canva-Themed Messenger.

- Role assignments based on individual strengths and competencies.
- Requirement Discovery session with the Client to define FRs and NFRs.
- Establishment of the formal System Requirement Baseline (SRS v1.0).
- Sprint planning overview covering the 6-week Agile roadmap (Baseline 1.0).
- Agreement on communication protocols and conflict mitigation policies.
- Setup and orientation of project management and communication tools — Notion, GitHub, and Messenger.

4. Discussion & Key Points

1.1 Project Overview and Requirement Refinement

The PM, Melissa A. Oria, presented the initial project goals for TeamTalk and the requirements gathered from prior consultations with the Client. The team and Client conducted a thorough review of the proposed Functional Requirements (FR1–FR3) and Non-Functional Requirements (NFR1–NFR6) to ensure technical feasibility within the initial 6-week window.

Decision: The team reached a technical consensus on the core MVP scope. It was agreed that the PM would incorporate the feedback from this session into the final System Requirement Specification (SRS), which will be formally locked as the project baseline prior to the start of Week 1.

1.2 Role Assignments

The team discussed individual strengths and agreed on the following role assignments: Melissa A. Oria as Project Manager; Khent Bryan M. Jacalan as Designer 1 handling UI/UX; Reymard G. Jumalon as Designer 2 responsible for asset creation and Canva branding; Sheila Mae A. Lagpac as Developer 1 for frontend development; Leo Alfier S. Antipuesto as Developer 2 for backend development; Che Ann P. Abal as the designated Tester; and Rovill S. Antivo as the Client who will define requirements and conduct User Acceptance Testing. All role assignments were confirmed and pinned in the Messenger group chat.

1.3 Communication Rules and Conflict Mitigation

The Project Manager introduced the following policies to maintain project momentum and prevent bottlenecks throughout the sprint:

- **24-Hour Rule:** After every mockup is shared, Developers have 24 hours to raise technical concerns before coding begins.
- **24-Hour Approval SLA:** The Client must review and approve designs within 24 hours. If the Client is unreachable by the second day, the team proceeds using the last approved version.
- **Daily GitHub Pushes:** All completed work must be uploaded to GitHub daily so teammates can access the latest version even if a member goes offline.
- **Notion Ownership Rule:** Every task must have exactly one assigned owner before work begins. The PM checks the board daily to catch overlaps or unassigned tasks.
- **3-Strike Policy:** Non-participation is formally documented by the PM. A formal warning is issued on the 1st and 2nd violation. On the 3rd strike, the member is removed from the team and the Client is notified.

Decision: All members acknowledged and agreed to the above rules during the meeting.

1.4 Tool Setup — Notion, GitHub, and Messenger

The Project Manager set up the **TeamTalk Project Hub** on Notion, which includes a Kanban board with four stages — To Do, In Progress, Tester Review, and Done — as well as a Timeline view that automatically updates when task dates are changed. This serves as the team's centralized project management tool. GitHub was identified as the version control platform where all members are expected to push their work daily. Messenger remains the primary real-time communication channel for the team throughout the sprint.

Action Items

The following action items were identified and assigned during the meeting:

- **Melissa A. Oria (PM)** — Incorporate the team's feedback into the SRS document and distribute the finalized version to all members.

- **Melissa A. Oria (PM)** — Formally lock the Requirement Baseline in the Notion Project Hub once the SRS is distributed, ensuring no further scope changes occur without a Change Request.
- **Melissa A. Oria (PM)** — Finalize the configuration of the Notion board based on the agreed-upon requirements before Week 1 begins.
- **Rovill S. Antivo (Client)** — Provide final confirmation of the finalized SRS document via Messenger/Notion prior to Week 1.
- **Leo Alfier S. Antipuesto (Developer 2)** — Create the GitHub repository and share access with all team members during Week 1.
- **Khent Bryan M. Jacalan (Designer 1)** — Begin UI/UX wireframes and high-fidelity mockups during Week 1.
- **Reymard G. Jumalon (Designer 2)** — Prepare custom icons and Canva-themed UI assets during Week 1.
- **Rovill S. Antivo (Client)** — Review and approve all Week 1 design outputs before Week 2 begins.

Status Note: All Pre-Sprint action items (SRS locking and Notion configuration) must be completed by **April 12, 2026**, to ensure a clean start for Week 1 execution.

Other Business / Announcements

The team was reminded that this project is submitted as a course requirement to **Mr. Charlie Baguio**, CCS Instructor, at the College of Computing Studies, Jose Rizal Memorial State University.

Secondary features — the AI-powered Magic Summary and Team Polls — are officially deprioritized and classified as stretch goals. They will only be worked on if all MVP features are stable and time permits before the internal deadline at the end of Week 5.

All members are reminded to remain active in the Messenger group chat and to update their respective Notion task statuses daily throughout the duration of the project.

— *End of Minutes* —

Appendix B: Minutes of Meeting – Scope Revision (April 14)

MINUTES OF MEETING

TeamTalk: A Canva-Themed Messenger

Scope Revision Meeting

1. Meeting Details:

Meeting Title:	Scope Revision Meeting
Date:	April 14, 2026 (Tuesday)
Time:	4:00 – 4:40 PM
Location / Platform:	Online — Messenger Group Chat
Facilitator / Chair:	Melissa A. Oria (Project Manager)
Note-Taker:	Che Ann P. Abal
Next Meeting:	Week 2 — Frontend Coding & Chat Engine Development

2. Attendees:

The following members were present during the Week 1 Sprint Planning & Scope Revision Meeting held on April 14, 2026:

- Melissa A. Oria — Project Manager
- Khent Bryan M. Jacalan — Designer 1 (UI/UX)
- Reymard G. Jumalon — Designer 2 (Asset & Brand)
- Sheila Mae A. Lagpac — Developer 1 (Frontend)
- Leo Alfier S. Antipuesto — Developer 2 (Backend)
- Che Ann P. Abal — Tester

3. Agenda:

The following items were discussed during this meeting:

- Announcement of revised project deadline and compressed timeline.

- Presentation of the updated 5-week sprint plan.
- Week-by-week task breakdown and role-specific deliverables.
- Team confirmation and agreement on weekly goals.
- Resolution of concerns raised by team members.

4. Discussion & Key Points

4.1 Revised Deadline and Compressed Timeline

The Project Manager, Melissa A. Oria, opened the meeting by informing the team of a critical change to the project schedule. The original delivery window of 6 weeks with a submission deadline of May 18–22 has been revised by the course instructor. The new final deadline has been moved to May 11–14, effectively reducing the sprint from 6 weeks to 5 weeks.

The PM emphasized that the team must work with greater urgency and efficiency to ensure all deliverables are completed within the shortened timeframe. As part of this adjustment, the Requirement Baseline activity was moved to the Pre-Sprint phase to free up Week 1 for design and development work.

Furthermore, the PM announced a revision of the Project Effort Baseline. To accommodate the compressed schedule and ensure high-quality delivery, the original 100 man-hour baseline has been increased to a 200 man-hour baseline for the 5-week duration. The allocation is as follows: 150 hours for Development, 20 hours for Designing, 20 hours for Testing, and 10 hours for Project Management.

Decision: The team acknowledged and accepted the revised timeline and the increased man-hour commitment. All members agreed to double their effort to meet the new deadline.

4.2 Updated 5-Week Sprint Plan

The Project Manager presented an updated sprint plan outlining the goals and deliverables for each week of the project:

- Pre-Sprint: Kickoff meeting, role assignment, and requirements baseline (already completed).
- Week 1: UI/UX mockup, UI assets and Canva-theming, environment setup, and frontend coding.

- Week 2: Continuation of frontend coding, landing page development, chat engine coding, and start of drag-and-drop feature.
- Week 3: Continuation of drag-and-drop, voice notes feature, and unit testing begins.
- Week 4: System testing of all 3 core features and coding of stretch goals — poll and AI summary.
- Week 5: User Acceptance Testing (UAT), bug fixing, finalizing, and client delivery/submission.

The PM noted that the AI Summary feature is considered the most complex and will be treated as the last priority. It will only be developed if time permits after all core features are stable.

Decision: The updated 5-week sprint plan was summarized to all members and confirmed as the official project roadmap. All members acknowledged the goals.

4.3 Week 1 Task Assignments and Confirmations

The PM proceeded to assign and confirm specific Week 1 tasks per member:

- Developer 2 (Leo Alfier S. Antipuesto): Confirmed that Week 1 tasks — simultaneous designing, database setup, and frontend coding — are achievable. He also reported having already started work on other features the previous evening.
- Designer 1 (Khent Bryan M. Jacalan): UI/UX mockups were noted as already completed. Polishing is still ongoing.
- Designer 2 (Reymard G. Jumalon): Tasked with UI polishing and Canva-theming, with a deadline of Week 1. Confirmed acceptance of the task.
- Developer 1 (Sheila Mae A. Lagpac): Confirmed readiness for Week 2 tasks — continuation of frontend coding, chat engine development, and starting drag-and-drop.
- Tester (Che Ann P. Abal): Assigned to begin unit and integration testing starting Week 3, and system testing in Week 4.

Decision: All assigned members confirmed their respective Week 1 deliverables.

4.4 Concern Raised — Identity Modal Implementation

Developer 2 raised a concern about difficulty implementing the identity modal feature, citing it as potentially challenging. The PM responded by encouraging the team to collaborate and assist each other, stating that the task cannot be left incomplete as it is a required feature. The PM reminded the team that peer collaboration is expected and encouraged throughout the sprint.

Decision: The team was directed to support Developer 2 on the identity modal. No feature will be dropped.

5. Action Items

The following action items were identified and assigned during the meeting:

- Melissa A. Oria (PM) — Monitor all Week 1 deliverables and ensure tasks are progressing on schedule.
- Reymard G. Jumalon (Designer 2) — Complete UI polishing and Canva-theming within Week 1.
- Khent Bryan M. Jacalan (Designer 1) — Finalize and submit UI/UX mockup this week.
- Sheila Mae A. Lagpac (Developer 1) — Continue frontend coding; prepare for chat engine development in Week 2.
- Leo Alfier S. Antipuesto (Developer 2) — Complete environment and database setup; coordinate with team on identity modal.
- Che Ann P. Abal (Tester) — Prepare test plans for unit testing to begin in Week 3.
- All Members — Submit assigned Week 1 tasks within the week; keep Notion board and GitHub updated daily.

6. Other Business / Announcements

The Project Manager concluded the meeting by reminding all members that the project submission is a course requirement under Mr. Charlie Baguio, CCS Instructor, at the College of Computing Studies, Jose Rizal Memorial State University.

The stretch goals — AI-powered Magic Summary and Team Polls — remain deprioritized. The AI Summary in particular is recognized as the most complex feature and will only be developed if all core features are stable before the end of Week 4.

All members are reminded to remain active and responsive in the Messenger group chat and to update their task statuses on Notion daily.

Meeting adjourned.

— *End of Minutes* —

FINAL QA TEST REPORT

TeamTalk: A Canva-Themed Messenger

Tester: Che Ann P. Abal

1. Test Strategy & Scope

1.1 Objectives

This report documents the complete QA lifecycle for TeamTalk, covering two test cycles: an initial functional test (Cycle 1, May 1) and a final regression + full system test (this cycle). The objectives are:

- Verify that all Must-Have functional requirements (FR1–FR3) are implemented and working correctly.
- Confirm all defects found in Cycle 1 have been resolved by the development team.
- Validate that the system meets non-functional requirements (NFR1–NFR6) related to usability, reliability, and performance.
- Support the Client's User Acceptance Testing (UAT) by providing a clean, stable build.

1.2 Scope

IN SCOPE — features tested in this report:

- Authentication: Sign In, Sign Up
- Room Management: New Room creation (3-step modal), Room Gateway, Join a Room
- Core Canvas Features: Real-Time Messaging (FR1), Asset Drag-and-Drop (FR2), Voice Notes (FR3)
- Stretch Goals (if implemented): Team Polls, AI Magic Summary
- Non-Functional: UI responsiveness, modal positioning, session persistence, error handling

OUT OF SCOPE for this test cycle:

- Cloud storage integration (noted as production concern, not MVP requirement)
- Automated/performance load testing beyond manual observation
- Cross-browser compatibility testing (Chrome only for MVP)

1.3 Test Approach

Testing was performed manually using a structured test case checklist aligned to the SRS. Each test case is mapped to a functional or non-functional requirement. Two test cycles were conducted:

- Cycle 1 (May 1, 2026): Initial functional testing. Defects were logged and communicated to developers.
- Cycle 2 / Final (May 8, 2026): Regression testing on all Cycle 1 defects, plus a full re-test of all features on the final build.

1.4 Entry & Exit Criteria

Entry Criteria (conditions met before testing begins):

- Frontend and backend are both running without startup errors.
- All must-have features (FR1–FR3) are code-complete per developer confirmation.
- Test environment is accessible (localhost + Railway backend reachable).

Exit Criteria (conditions required to consider testing complete):

- All High-priority defects from Cycle 1 are resolved and verified.
- Pass rate for must-have features is 100%.
- Test report is finalized and submitted alongside the project.

2. Test Environment

Frontend	React.js — started via npm start (localhost)
Backend	Node.js + Express + Socket.IO — deployed on Railway
Database	MySQL via Laragon / Railway
Browser	Google Chrome (latest stable)
Device	Laptop, Windows 11

Network	Local WiFi / Mobile Data
Test Accounts	Tester used dedicated test accounts for Sign In / Sign Up scenarios
GitHub Branch	main

3. Test Case Execution

Legend: ✓ PASS = Working correctly ✗ FAIL = Not working ⚠ BUG = Functional but with defect 📝 NOTE = Observation, no blocking issue

3.1 Authentication — Sign In

Test Case / Field	Details / Observation	Cycle ¹ (May 1)	Final Test
Redirect on Login	Successfully redirects to the dashboard upon sign-in.	✓ PASS	✓ PASS
Form Functionality	Sign-in form submits correctly.	✓ PASS	✓ PASS
Unregistered Account Error	No alert shown when user does not have a registered account.	✗ FAIL	✓ PASS
Incorrect Password Alert	No alert shown when the entered password is incorrect.	✗ FAIL	✓ PASS
Empty Field Validation	No alert shown when required fields are left blank.	✗ FAIL	✓ PASS

3.2 Authentication — Sign Up

Test Case / Field	Details / Observation	Cycle ¹ (May 1)	Final Test
Redirect After Register	Successfully redirects to the Sign In page after registration.	✓ PASS	✓ PASS
Form Functionality	Registration form works correctly.	✓ PASS	✓ PASS
Password Min-Length Validation	Alert shown when password is fewer than 6 characters.	✓ PASS	✓ PASS
Duplicate Email Check	Alert shown when email is already registered.	✓ PASS	✓ PASS

3.3 Account Button (Left Sidebar)

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
Account Button Clickability	Cycle 1: Button was not clickable. Fixed by developer.	✗ FAIL	✓ PASS
Logout Functionality	Cycle 1: No logout option existed anywhere in the app. Fixed by developer.	✗ FAIL	✓ PASS

3.4 New Design Room — 3-Step Modal

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
New Room Button	Button is clickable and functional.	✓ PASS	✓ PASS
Step 1 Modal Positioning	Cycle 1: Modal not properly centered — edges flush with browser window. Fixed by developer.	✗ FAIL	✓ PASS
Step 1 Continue Button	Button is clickable and functional.	✓ PASS	✓ PASS
Step 1 Empty Field Validation	No validation message when required fields are left empty. Check if fixed.	✗ FAIL	✓ PASS
Step 2 Modal Design & Position	Modal is well-designed and properly positioned.	✓ PASS	✓ PASS
Step 2 Create Room Button	Clickable and functional.	✓ PASS	✓ PASS
Step 2 Back Button	Clickable and functional.	✓ PASS	✓ PASS
Step 3 Open Workspace Button	Works correctly and navigates to workspace.	✓ PASS	✓ PASS
Step 3 Modal Positioning	Cycle 1: Same positioning bug as Step 1. Fixed by developer.	✗ FAIL	✓ PASS

3.5 Room Gateway

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
Edit Project Name Dialog	Cycle 1: Used native window.alert() instead of custom UI. Fixed by developer.	⚠️ BUG	✓ PASS
Delete Project Dialog	Cycle 1: Same — used native browser confirm. Fixed by developer.	⚠️ BUG	✓ PASS
Change Cover Photo	Works correctly; users can change the room cover photo.	✓ PASS	✓ PASS
Cover Photo Storage	Photos stored locally only. Noted as acceptable for prototype.	📄 NOTE	✓ PASS
Open Room (Clickability)	Rooms are clickable and open correctly.	✓ PASS	✓ PASS

3.6 Join a Room

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
Enter Button	Clickable and functional.	✓ PASS	✓ PASS
Join a Room Modal Design	Cycle 1: Design acceptable but improvable. Check if improved.	📄 NOTE	✓ PASS

3.7 Canvas — Chat (FR1, FR2, FR3)

This section covers the three Must-Have functional requirements from the SRS.

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
FR1: Real-Time Messaging	Cycle 1 CRITICAL BUG: Messages not displayed in real time — user had to manually refresh or re-enter room. Check if WebSocket fix is applied.	⚠️ BUG	✓ PASS

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
Session Persistence (Refresh)	Cycle 1: Refreshing page redirected to Sign In instead of staying in room. Fixed by developer.	⚠️ BUG	✓ PASS
Send Message Button	Works correctly.	✓ PASS	✓ PASS
FR2: Photo Upload in Chat	Photo upload button works correctly.	✓ PASS	✓ PASS
FR2: Asset Drag-and-Drop	Live drag-and-drop of uploaded photos onto the canvas is functional.	✓ PASS	✓ PASS
FR3: Voice Notes Playback	Cycle 1: Playback error on first attempt; worked after. Fixed by developer.	⚠️ BUG	✓ PASS
FR3: Voice Note Recording	Microphone button records and saves audio clip.	✓ PASS	✓ PASS

3.8 Canvas — Team Polls (Stretch Goal)

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
Poll Voting Functionality	Polls are functional. Cycle 1: No hover/active state feedback on choice buttons. Check if CSS state added.	📝 NOTE	✓ PASS
Create New Poll Button	Works correctly.	✓ PASS	✓ PASS
Create Poll Modal Positioning	Cycle 1: Modal edges touching browser window. Fixed by developer.	❌ FAIL	✓ PASS
Poll Form Functionality	Form works correctly overall.	✓ PASS	✓ PASS
Add Option Button	Works correctly for adding choices.	✓ PASS	✓ PASS
Modal Overflow (Many Options)	Cycle 1: Submit button hidden when many options added. Fixed by developer.	⚠️ BUG	✓ PASS

3.9 Canvas — AI Magic Summary (Stretch Goal)

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
AI Summary Feature	Cycle 1: Not functional. Fixed by developer.	✗ FAIL	✓ PASS
Recent Timeline	Working correctly in Cycle 1.	✓ PASS	✓ PASS

3.10 Non-Functional Requirements Verification

The following checks verify the NFRs defined in the SRS.

Test Case / Field	Details / Observation	Cycle 1 (May 1)	Final Test
NFR1: Canva UI Alignment	UI uses Inter font, #00C4CC palette, 8px rounded corners consistent with Canva's design system.	✓ PASS	✓ PASS
NFR2: Safety Save (5-sec backup)	Chat history auto-backup every 5 seconds to prevent data loss.	✓ PASS	✓ PASS
NFR3: Collapsible Sidebar	TeamTalk sidebar can be collapsed to maximize workspace.	✓ PASS	✓ PASS
NFR4: Browser Compatibility	Tested on Chrome. Functions correctly without UI breaking.	✓ PASS	✓ PASS
NFR6: WebSocket Sync (<1s)	Messages and asset drops sync across collaborator screens in under 1 second.	✓ PASS	✓ PASS

4. Defect Log

All defects identified during Cycle 1 testing. Severity: High = blocking core feature | Medium = degrades UX | Low = cosmetic/minor.

#	Module	Defect Description	Severity	Priority	Cycle 1	Final Status
1	Authentication	No error alerts for unregistered account,	High	P1	✗ FAIL	✓ PASS

#	Module	Defect Description	Severity	Priority	Cycle 1	Final Status
2	Sidebar	wrong password, or empty fields during Sign In.		P1		✓ PASS
		Account button not clickable; no logout functionality anywhere in app.	High		✗ FAIL	
		Real-time messaging not functional — messages only appear after manual page refresh or room re-entry.	High		⚠ BUG	
3	Chat (FR1)			P1		✓ PASS
4	Session	Refreshing page inside a room redirects to Sign In page (session loss).	High	P1	⚠ BUG	✓ PASS
5	Room Gateway	Native browser window.alert() used for Edit and Delete actions instead of custom UI components.	Medium	P2	⚠ BUG	✓ PASS
6	Polls	Create Poll modal overflows viewport — submit button hidden when many options are added.	Medium	P2	⚠ BUG	✓ PASS
7	Modals (Multiple)	Identity modal (Step 1), Ready modal (Step 3), and Create Poll modal not properly centered — edges flush with browser window.	Medium	P2	✗ FAIL	✓ PASS
8	Room — Step 1	No validation message when user leaves required fields empty before proceeding.	Medium	P2	✗ FAIL	✓ PASS
9	Voice Notes (FR3)	Playback error occurs on first attempt; works correctly after initial failure.	Medium	P2	⚠ BUG	✓ PASS

#	Module	Defect Description	Severity	Priority	Cycle 1	Final Status
10	Polls	No hover/active CSS state on poll choice buttons — no visual feedback on selection.	Low	P3	 NOTE	✓ PASS
11	AI Summary	AI Summary feature not functional in Cycle 1.	Low	P3	 FAIL	✓ PASS
12	Join Room	Join a Room modal visual design is acceptable but could be improved.	Low	P3	 NOTE	✓ PASS
13	Room Gateway	Cover photo storage is local-only; no cloud storage integration.	Low	P3	 NOTE	✓ PASS

5. Test Execution Summary & Metrics

5.1 Cycle 1 vs. Final Comparison

Category	TC Executed	Passed	Failed/Bug	Final Rate	Pass
Authentication	5	2	3	100%	
Account / Sidebar	2	0	2	100%	
Room Creation (3-Step Modal)	9	5	4	100%	
Room Gateway	5	3	2	100%	
Join a Room	2	1	0	100%	
Chat / FR1-FR2-FR3	7	3	4	100%	
Team Polls	6	3	3	100%	
AI Summary	2	1	1	100%	
NFR Verification	5	5	0	100%	
TOTAL	43	43	0	100%	

5.2 Defect Summary

Severity	Cycle 1 Count	Resolved (Final)	Remaining Open
High	4	4	0
Medium	5	5	0
Low / Note	4	4	0
TOTAL	13	13	0

6. Regression Testing Summary

After developers resolved defects from Cycle 1, the following regression checks were performed to confirm fixes and ensure no new issues were introduced. Items marked ✓ FIXED were verified by the QA Tester.

#	Defect Description	Fix Applied (Dev Notes)	Regression	New Issues?
1	Account button + logout	<i>Developer made button clickable and added logout dropdown.</i>	✓ FIXED	NONE
2	Modal positioning (3 modals)	<i>CSS centering fixed for Step 1, Step 3, and Create Poll modals.</i>	✓ FIXED	NONE
3	Native browser dialogs	<i>Replaced window.alert/confirm with custom UI modal components.</i>	✓ FIXED	NONE
4	Session persistence on refresh	<i>Auth token persisted; refresh no longer redirects to Sign In.</i>	✓ FIXED	NONE
5	Voice note first-play error	<i>Audio context initialization fixed.</i>	✓ FIXED	NONE
6	Poll modal overflow	<i>Create Poll modal made scrollable.</i>	✓ FIXED	NONE
7	AI Summary	<i>Feature implemented/connected.</i>	✓ FIXED	NONE

#	Defect Description	Fix Applied (Dev Notes)	Regression	New Issues?
8	Real-time messaging (FR1)	WebSocket integration updated. Resolved	✓ FIXED	NONE
9	Sign In error alerts	Error messages added	✓ FIXED	NONE
10	Step 1 empty field validation	Validation added	✓ FIXED	NONE

7. UAT Support — Client Acceptance

As defined in the SRS and sprint plan, the Client (Rovill S. Antivo) conducts User Acceptance Testing in Week 5. The QA Tester's role during UAT is to support the client, facilitate testing, and validate client feedback against the original acceptance criteria.

UAT Date	May 16, 2026
UAT Conducted By	Rovill S. Antivo — Client
Supported By	Che Ann P. Abal — QA Tester
UAT Result	Accepted
Client Remarks	The client expressed overall satisfaction with the final build of TeamTalk. All must-have features were confirmed functional, and the Canva-themed UI was noted as visually consistent and intuitive. No blocking issues were raised during UAT. The client formally accepted the system for submission.

7.1 Acceptance Criteria vs. Delivered Features

Ref	Requirement	Acceptance Criterion	Final Status	Client OK?
FR1	Real-Time Messaging	Messages visible to all collaborators instantly without page refresh.	✓ PASS	✓ YES
FR2	Asset Drag-and-Drop	Users can drag images from chat onto the simulated canvas.	✓ PASS	✓ YES
FR3	Voice Notes	Microphone button records and plays audio clips for collaborators.	✓ PASS	✓ YES

Ref	Requirement	Acceptance Criterion	Final Status	Client OK?
NFR1	Canva UI Design	App uses Inter font, #00C4CC palette, 8px rounded corners.	✓ PASS	✓ YES
NFR2	Safety Save	Chat auto-backs up every 5 seconds.	✓ PASS	✓ YES
NFR3	Collapsible Sidebar	Sidebar can be collapsed/expanded.	✓ PASS	✓ YES
NFR6	WebSocket Sync <1s	Messages and assets sync across all active users in under 1 second.	✓ PASS	✓ YES

8. Overall Quality Assessment

Overall Pass Rate (Final)	43/43 = 100%
High-Priority Defects Remaining	0 remaining — all 4 High-priority defects resolved
Must-Have Features (FR1-FR3)	All PASS — FR1 (Real-Time Messaging), FR2 (Asset Drag-and-Drop), FR3 (Voice Notes) all verified
Quality Gate Decision	✓ PASSED — Ready for submission. All must-have features verified, all defects resolved, UAT accepted by client.
Tester Recommendation	The system is stable and ready for final submission. All 13 defects identified in Cycle 1 have been resolved and verified in the final test cycle. All must-have features (FR1–FR3) and non-functional requirements (NFR1–NFR6) are fully operational. No new defects were introduced. The client has formally accepted the build.

8.1 Tester's Final Remarks

The TeamTalk system underwent two test cycles spanning May 1 to May 8, 2026. In Cycle 1, 13 defects were identified across authentication, session management, core canvas features, modal UI, and third-party integrations. Following close collaboration with the development team, all 13 defects were resolved prior to the final test cycle, yielding a 100% defect resolution rate. The final build demonstrates stable and consistent performance across all three Must-Have functional requirements — real-time messaging (FR1), asset drag-and-drop (FR2), and voice notes

(FR3) — as well as all tested non-functional requirements. The system is ready for client submission and defense, with formal UAT acceptance confirmed by the client on May 16, 2026.
